ಕಛೇರಿ ಪುಸ್ತಕ ಸಂಖ್ಯೆ: 4160/15-16

ಸದರಿ ಕಿರಿಕೆ ಪುಸ್ತಕವನ್ನು ಈ ದಿನಾಂಕದಲ್ಲಿ. ಜೆ
ಇಇ/ಎಇಇ/ಎಇ/ಜೆಇ/ಗುತ್ತಿಗೆದಾರರು ವಾರ್ಡ್ ನಂ 13 ಶೆಟ್ಟಿಹಳ್ಳಿ ದಿನಾಂಕ:
02/11/2016 ರಂದು ಎತ್ತಿರುವೆ. ಈ ಕಿರಿಕೆ ಪುಸ್ತಕವು
ಪುಟಸಂಖ್ಯೆ 415701 ರಿಂದ 416000 ರ ವರೆಗೆ ಕ್ರಮಬದ್ಧವಾಗಿ
ಪುಟಗಳನ್ನು ಹೊಂದಿದ್ದು ಮುಕ್ತಾಯಗೊಳಿಸಿದೆ.

EXECUTIVE ENGINEER
Bruhat Bangalore [illegible] Para Palike,
Dasarahalli Zone, Bangalore-57.
2/11/16

2/11/16

1st & final Bill

M. A. R. 57 (Rule 116)
Measurement Book

No. B 415901

Serial No. BR-06- dt 04-04-2016
Name of Work ..... From..... To.....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of work :- Modified Estimated for improvements & Asphalting to mallasandra main road Govt school to Anjaneya Swamy temple road, Mallsandra in ward No. 13 Shettyhalli Sub Division Est cost :- 25.00 Lakhs Job code No:- 013-13-000037 P code-2201 work order No:- EE/DD/ work order/447/12-13 dt 8.3.2013 Name of Agency:- Technical manager west KRIDL project implimentation unit						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	measurment recorded on 30-3-16						
	1) Earth work excavation by manual means ordinary soil involving an average horizontal throw upto 2 meters & an average lift upto 0.5m excavated surface leveled & sides neatly dressed the disposed earth to be leveled neatly after breaking of clods com -plete as per specification						
	Qty vide item No. 1 pre measurement recoded in pag no. 415969/2 of this MB					253.46	
	@Rs 65.98					65.88	16723.00
							16698.00

M. A. R. 57 (Rule 116)
Measurement Book

No. B 415902

Serial No. .....
Name of Work ..... From..... To.....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	3) providing, laying, spreading & compacting graded Stone aggregate to wet mix macadam specifications including premixing the material with water at OMC in mechanical mix plant carriage of mixed method of tipper to site laying in uniform layers with paver in sub base/base course on well prepared surface and compacting with vibratory roller to achieve the desired density complete as per specifications.						
	Qty vide item No. 3 premeasurement recorded on Page No. 415971 of this MB					226.22m3	
	@Rs 1121.04						Rs 3600.00

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
					BF	253.46	
						~~253.46~~ m3	
						7271	32456.00
	KRIDL charges	10%+1% Labours			Cess	~~20 13663=00~~	18429.00
		1885148=00					207200.07
		188515=00			Total =		2090837.07
		2073663=00					

Chd & Rec
30/3/16

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶಿಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು

Certified

30-3-16

M. A. R. 57 (Rule 116)

Measurement Book No. B 415908

2073663=00

Audited and admitted for Rs. 1800768=00

Passed by Cheque for Rs. 272895=00

Serial No. .....

Name of Work ..... From ..... To .....

Name of Contractor of na .....

Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	certifide that the work done satisfactarly						
	certifide that the debrise removed from the work spaces						

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶಿಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು

Certified

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

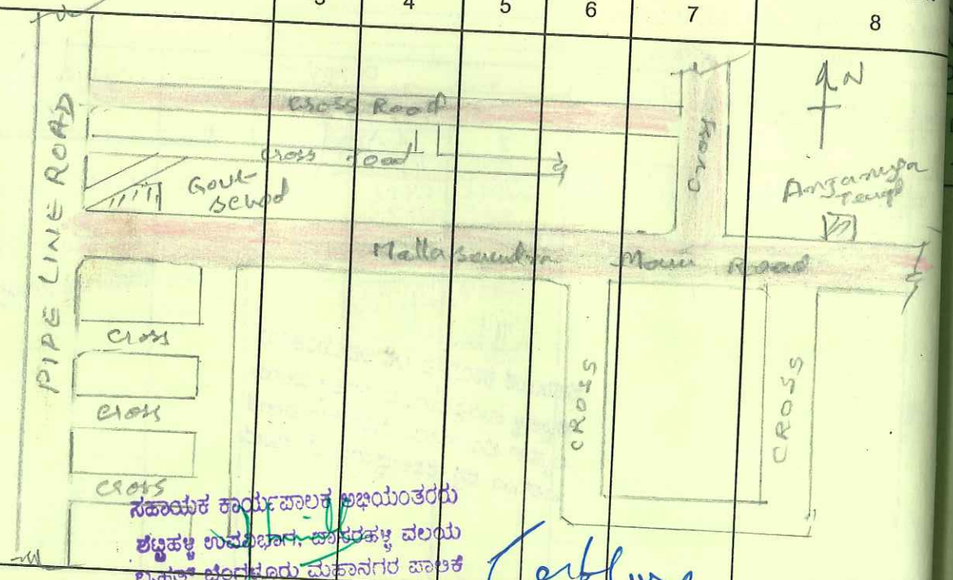

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶಿಟ್ಟಹಳ್ಳಿ ಉಪವಿಭಾಗ, ಜಾಲರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಕಛೇರಿ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.

Serial No. .....
Name of Work .....
Name of Contractor
Date of commencem

Date	Full desc
1	
